

Below is a summary of how we are progressing with the districts projects. These projects are possible due to community passage of the 2017 bond issue.

Site work and Athletic Fields

What Happened in January

- Engineering 75% complete.
- Foundations for Stadium complete.
- Plumbing underground.
- Electrical underground.




What's Coming in February

- Engineering completion for Athletics. Scoreboard / Lighting / Sound systems
- ALL on-site construction is weather dependent
- *Concession Building - masonry walls commence as weather permits.

Elementary and Central Energy Plant

What Happened in January

- CEP: Commissioning Mechanical systems.
- PRE; Punch work, big effort through Jan 4. Nearing 95% complete.
- PRE: Site work completion weather dependent.

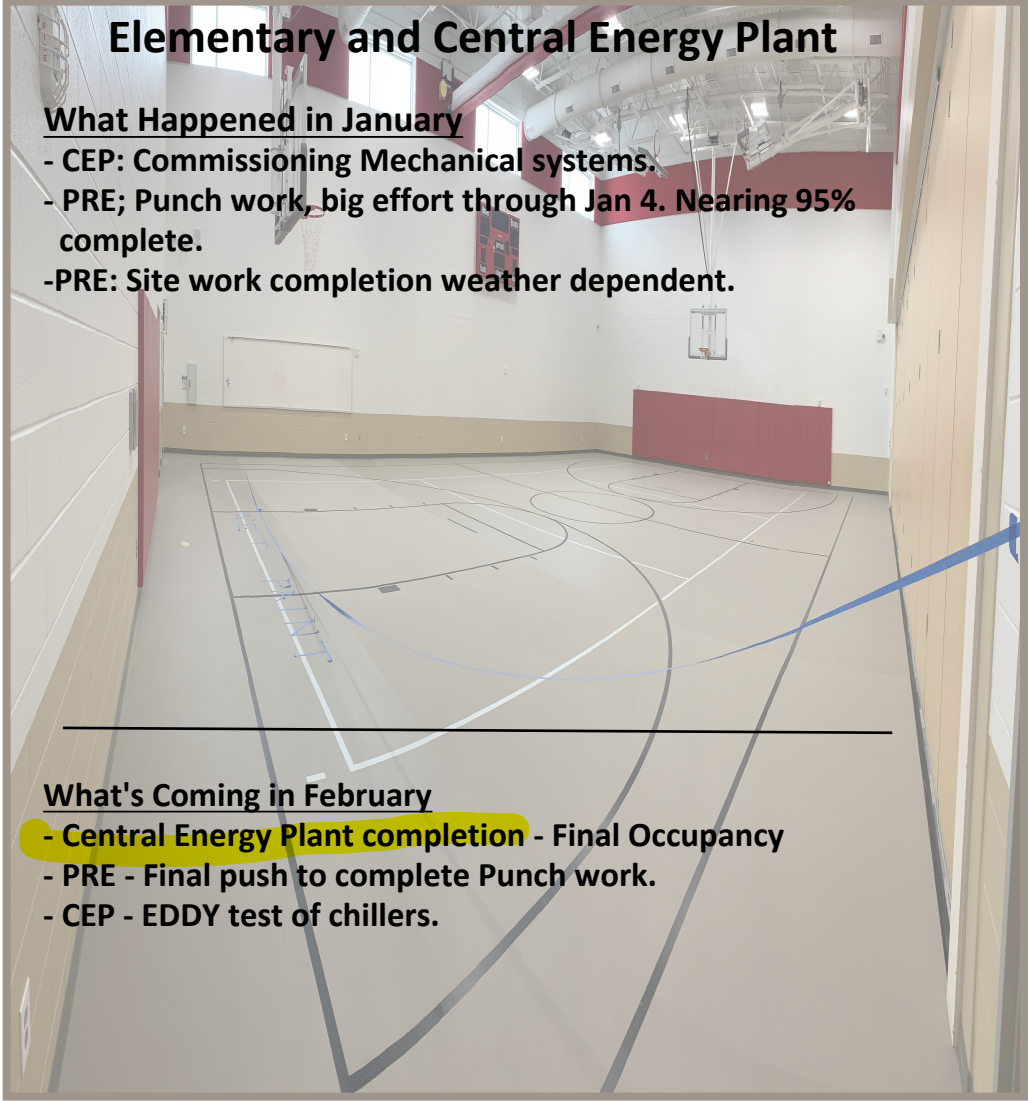


What's Coming in February

- Central Energy Plant completion - Final Occupancy
- PRE - Final push to complete Punch work.
- CEP - EDDY test of chillers.

High School


What Happened in January

- Structural Top-out of steel completes.
- ALL load bearing CMU complete.
- Area 3, 4, 5, 6, 8 roofing complete.
- Areas 2, 7 & 1 roofing installation partially installed.
- Area 3, 4 & 5 brick veneer complete.
- Area 6 & 7 brick veneer underway.
- Window frame installation in areas 3, 4 & 5 underway.
- CIP Slab on Grade scheduled for completion in January.
- Area 4, 5 & 6 level 1 & 2, Interior wall framing, Door frame installation, MEP rough in overhead and in wall complete.
- Area 4, 5 & 6, level 3 wall framing underway.
- Area 4 & 5, levels 1 & 2 drywall & drywall finishing underway.

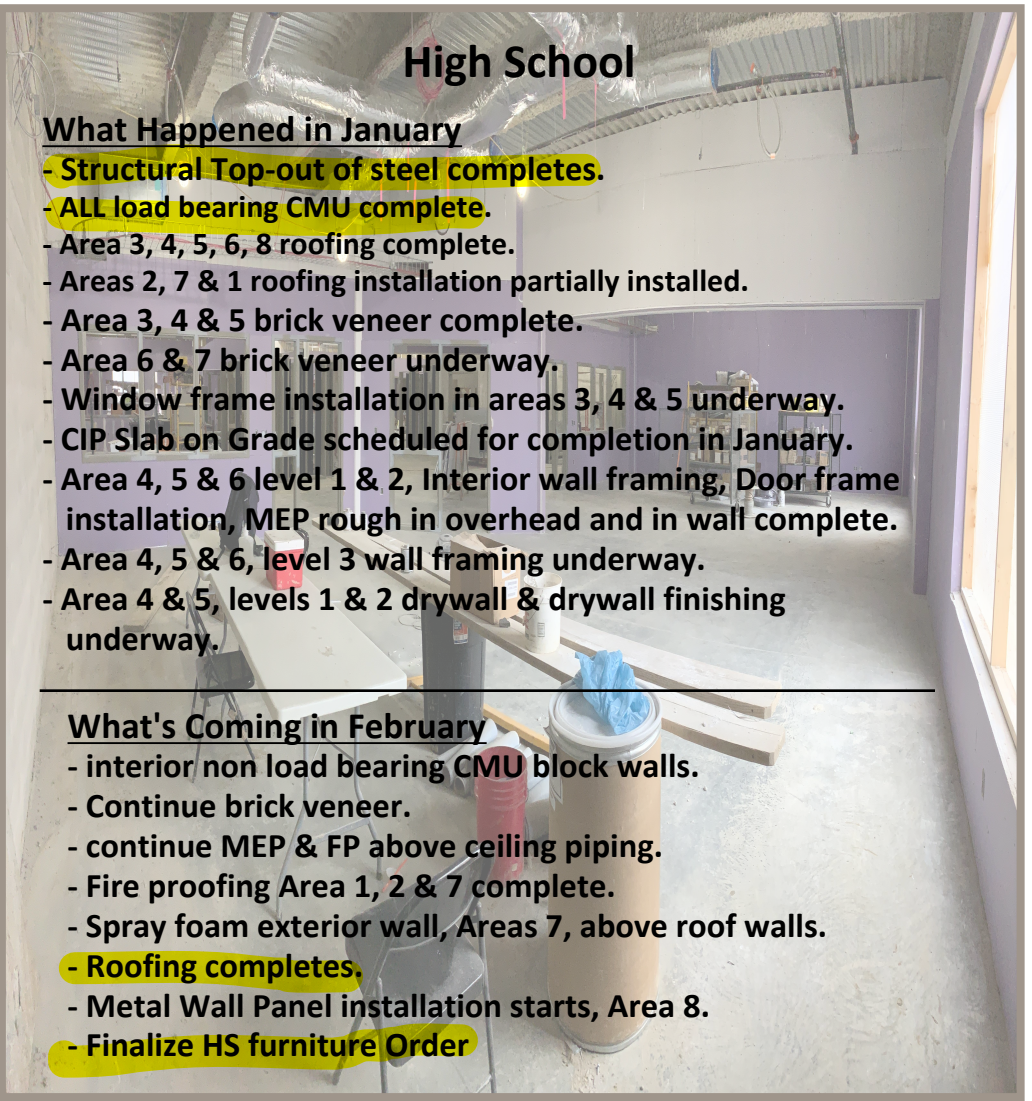

What's Coming in February

- interior non load bearing CMU block walls.
- Continue brick veneer.
- continue MEP & FP above ceiling piping.
- Fire proofing Area 1, 2 & 7 complete.
- Spray foam exterior wall, Areas 7, above roof walls.
- Roofing completes.
- Metal Wall Panel installation starts, Area 8.
- Finalize HS furniture Order

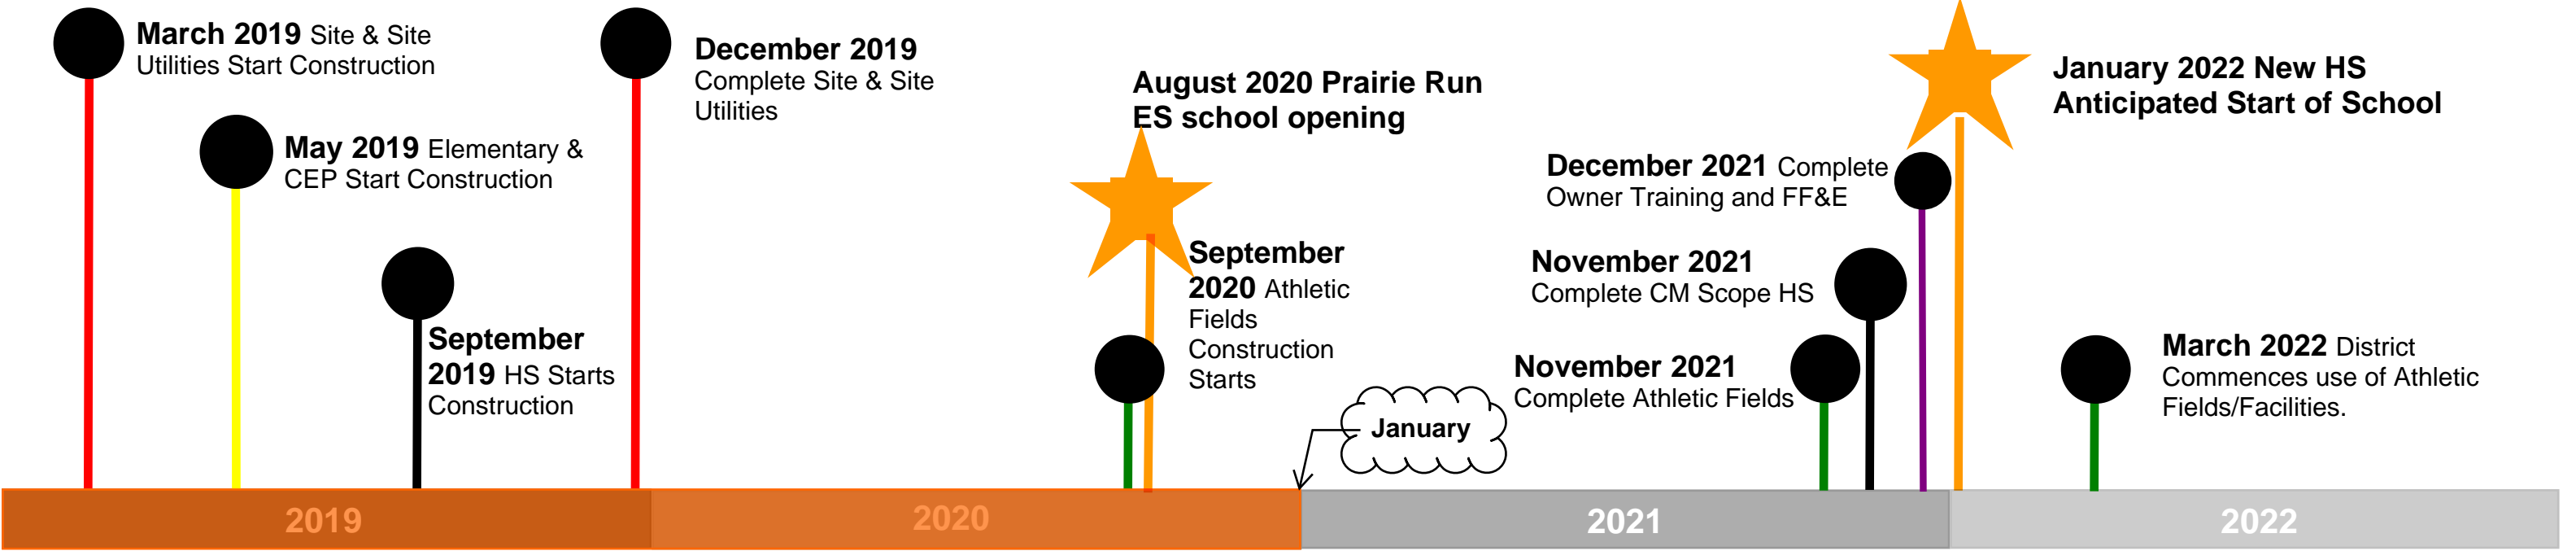

*Note: Final Elementary & HS completion/Move-in dates subject to change pending construction implementation/final inspections
