



BIG WALNUT LOCAL SCHOOLS PROJECT | Summary February 2021



Below is a summary of how we are progressing with the districts projects. These projects are possible due to community passage of the 2017 bond issue.

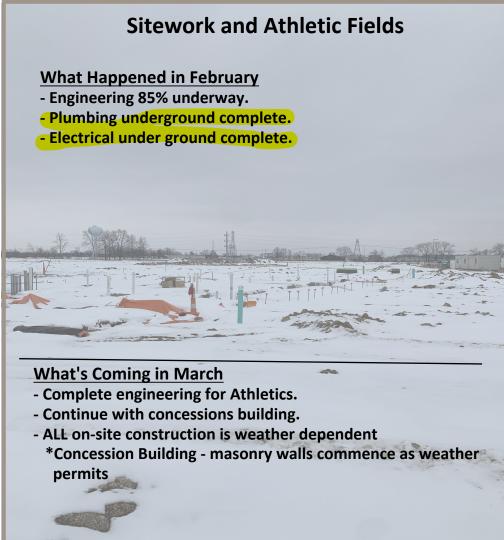


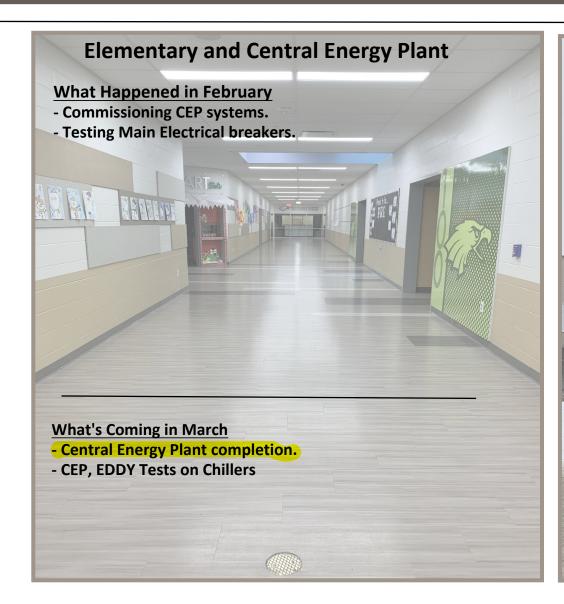

High School What Happened in February - Structural steel complete. - ALL load bearing CMU complete. - Area 3, 4, 5, 6, 8 roofing complete. - Areas 2, 7 & 1 roofing installation started. - Area 3, 4 & 5 brick veneer complete. - Area 6 & 7 brick veneer underway. - Window frame installation in areas 3, 4, 5 & 6 underway. - CIP Slab on Grade Area 1 toilet room area. - Area 4, 5 & 6 level 1 & 2, Interior wall framing, Door frame installation, MEP rough in overhead and in wall complete. - Area 4, 5 & 6, level 3 wall framing underway. - Area 4 & 5, levels 1 & 2 drywall & drywall finishing underway or complete. - Area 4, Primer & first coat of paint starts. What's Coming in March interior non load bearing CMU block walls. - Continue brick veneer. - Continue MEP & FP above ceiling piping. - Fire proofing Area 1, 2 & 7 complete.

- Spray foam exterior wall, Areas 7, above roof walls.

Roofing completion - weather dependent
 Metal Wall Panel installation starts, Area 8.

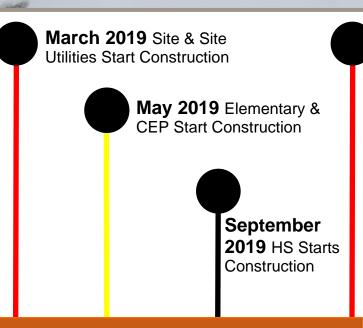

December 2019Complete Site & Site
Utilities



January 2022 New HS Anticipated Start of School

March 2022 District
Commences use of Athletic
Fields/Facilities.

2019 2020 2021 2022
