


Below is a summary of how we are progressing with the districts projects. These projects are possible due to community passage of the 2017 bond issue.

### Sitework and Athletic Fields

**What Happened in March**

- Engineering 95% complete.
- **Foundations complete.**
- **Initial designs for additional roadway underway**

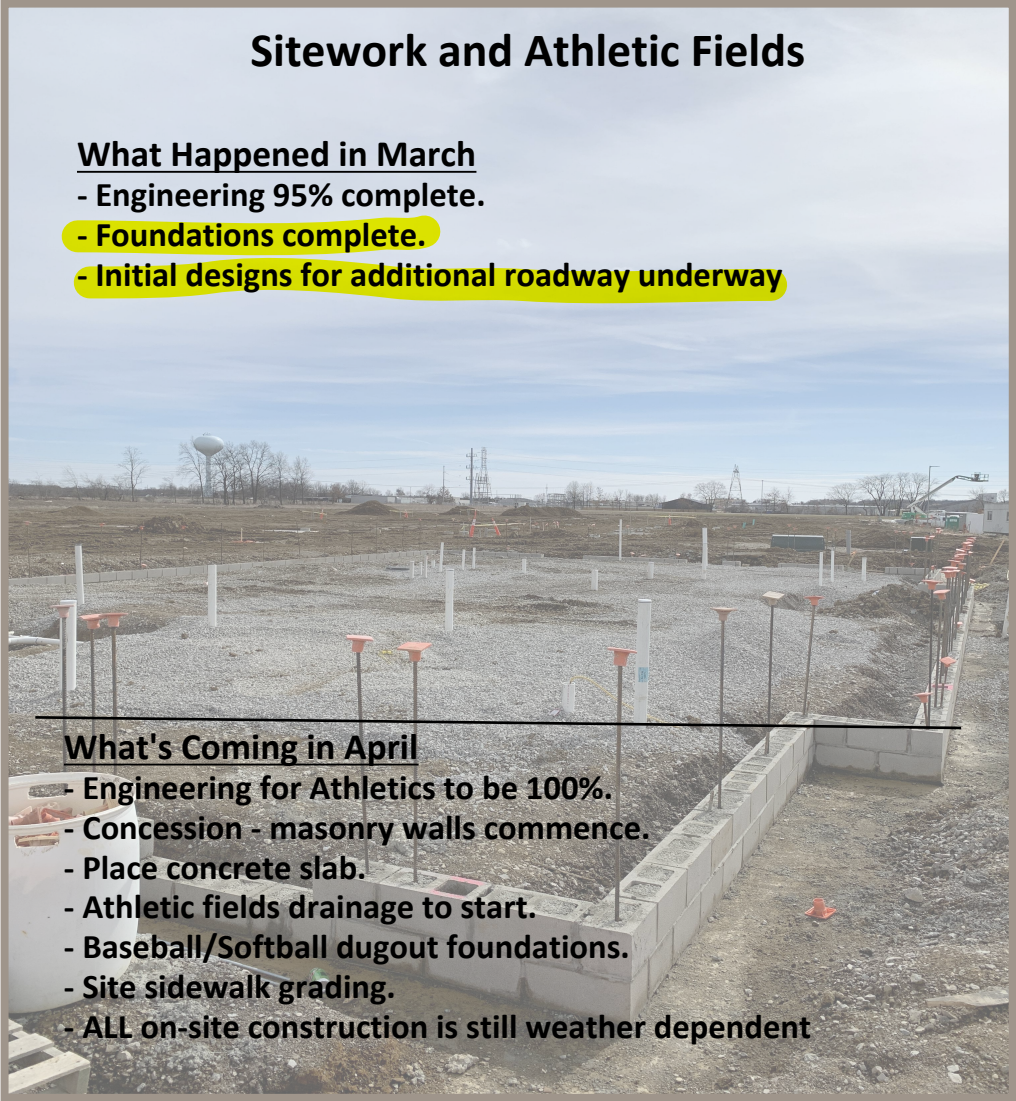


**What's Coming in April**

- Engineering for Athletics to be 100%.
- Concession - masonry walls commence.
- Place concrete slab.
- Athletic fields drainage to start.
- Baseball/Softball dugout foundations.
- Site sidewalk grading.
- ALL on-site construction is still weather dependent

### Elementary and Central Energy Plant

**What Happened in March**

- Commissioning CEP systems.
- Testing breakers.

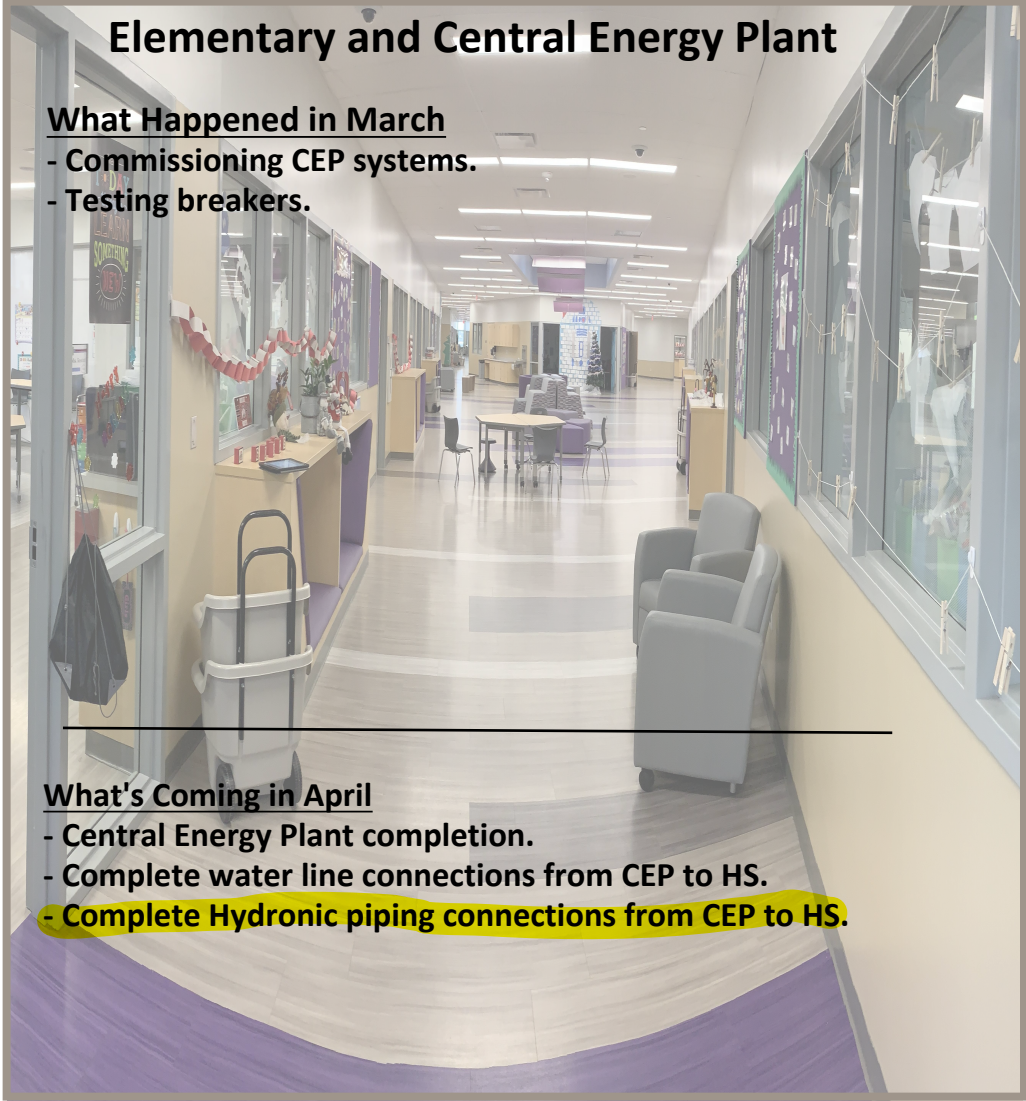


**What's Coming in April**

- Central Energy Plant completion.
- Complete water line connections from CEP to HS.
- **Complete Hydronic piping connections from CEP to HS.**

### High School


**What Happened in March**

- Stairs 4, 5 & 6 complete.
- Area 1, 2, 3, 4, 5, 6, 7, 8 flat roofing complete.
- Areas 2 & 7 sloped roof on going.
- Area 3, 4, 5, 6 & 7 brick veneer complete.
- Area 2 & courtyard brick veneer on going.
- Window frame installation in areas 3, 4, 5 & 6 underway.
- ALL CIP Slab on Grade complete.
- Area 4, 5 & 6 level 1 & 2, Interior wall framing, Door frame installation, MEP rough in overhead and in wall complete, drywall, drywall finishing complete.
- Area 4, 5 & 6, level 3 wall framing complete.
- Area 4 & 5, levels 1 & 2 Primer & first coat of paint on going.
- Area 4, level 1 & 2 ceiling grid installation on going.
- **Walk in cooler/Freezer & Kitchen Hood complete.**

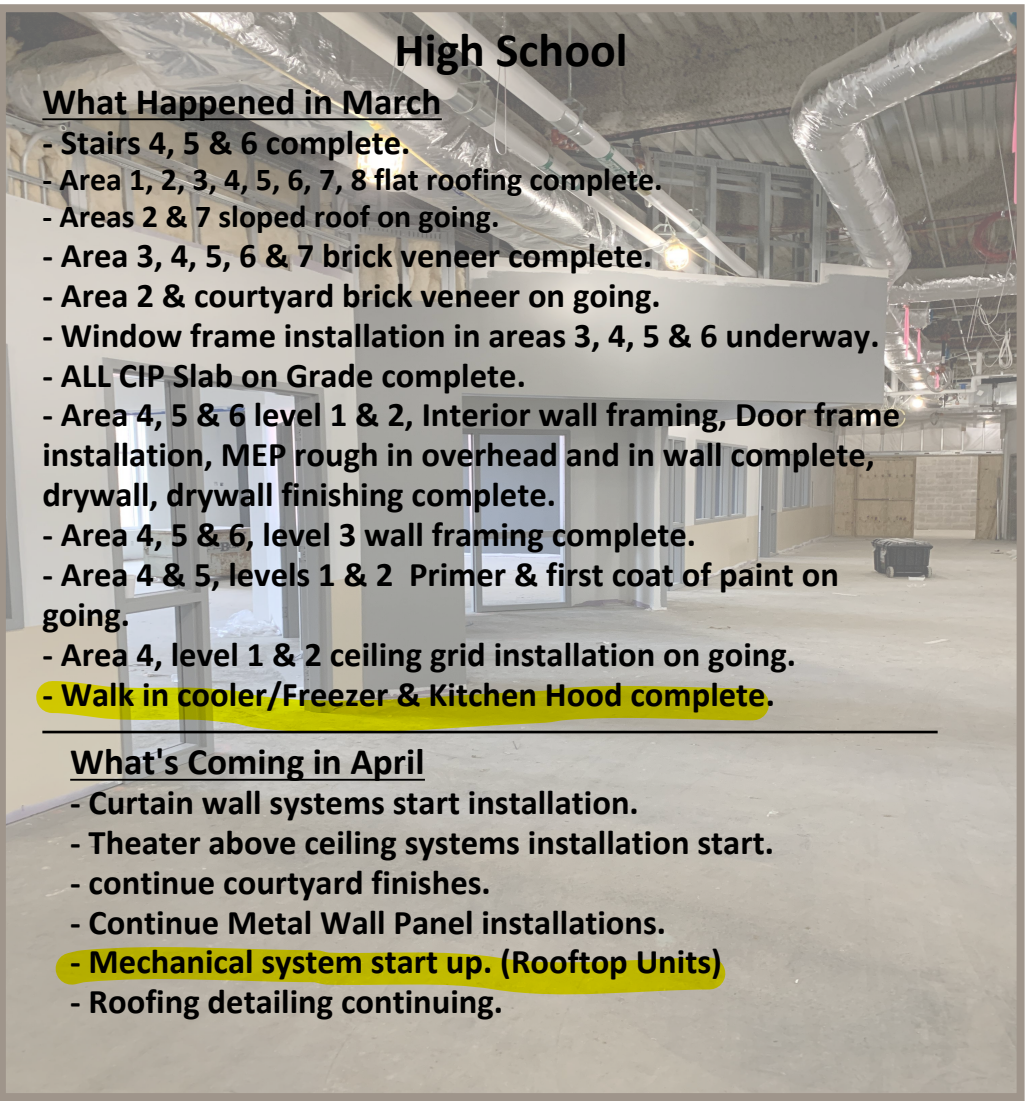

**What's Coming in April**

- Curtain wall systems start installation.
- Theater above ceiling systems installation start.
- continue courtyard finishes.
- Continue Metal Wall Panel installations.
- **Mechanical system start up. (Rooftop Units)**
- Roofing detailing continuing.

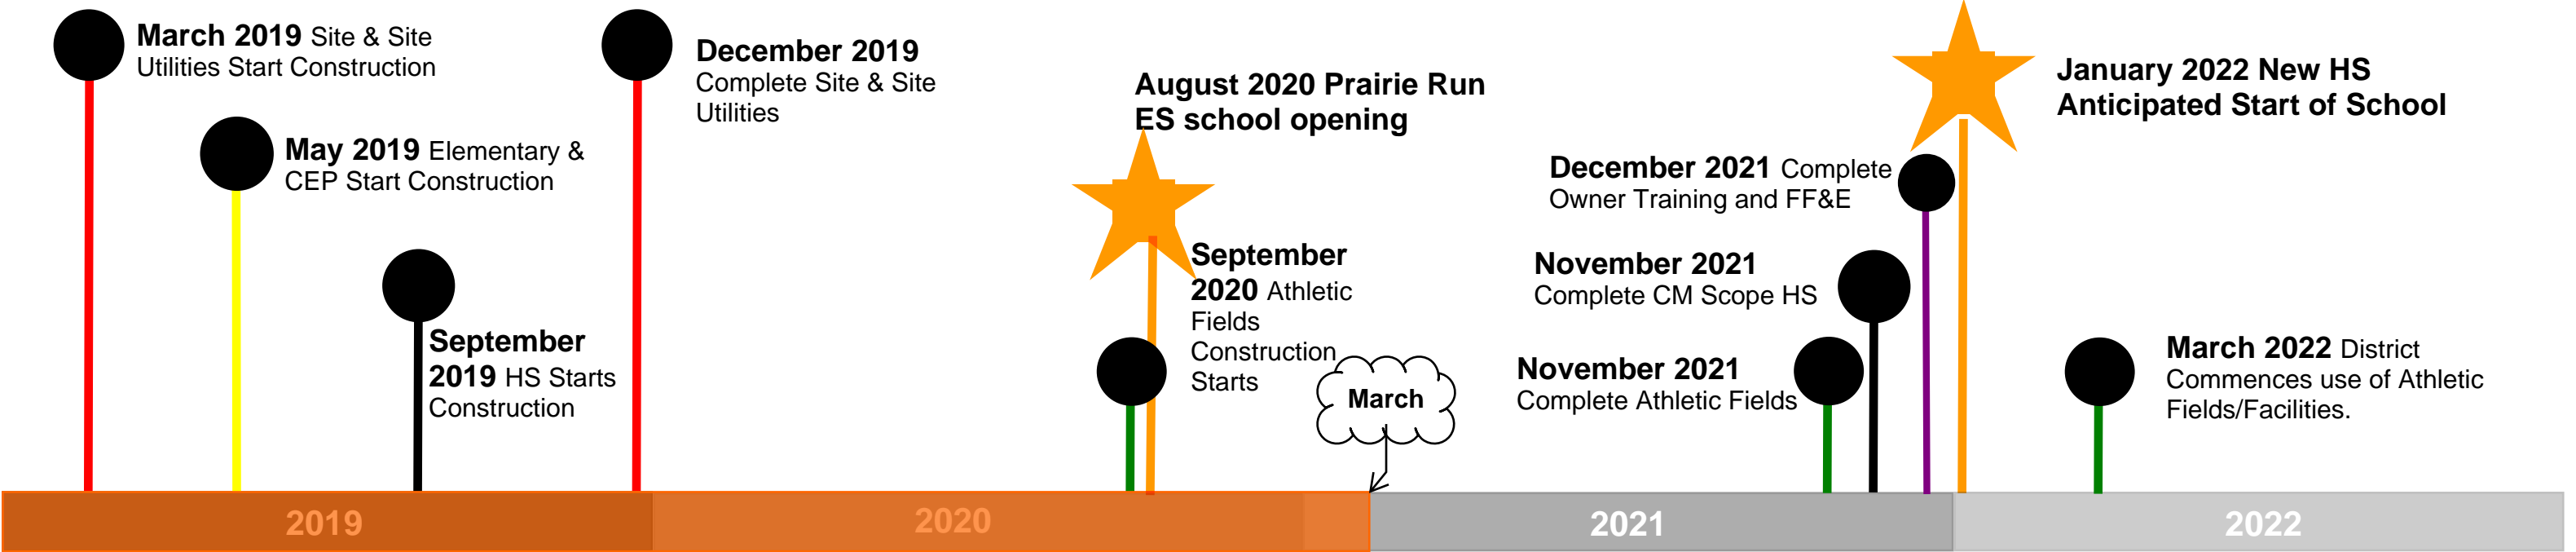

\*Note: Final Elementary & HS completion/Move-in dates subject to change pending construction implementation/final inspections
