

Below is a summary of how we are progressing with the districts projects. These projects are possible due to community passage of the 2017 bond issue.


Sitework and Athletic Fields

What Happened in April

- Engineering on going.
- Concessions Building Plumbing underground complete.
- Concessions Building Electrical under ground complete.
- Concessions Building Foundations complete.
- Prepare north loop road for asphalt.
- Start hard-scapes work at loading dock.

What's Coming in May

- Engineering for Athletics.
- Concessions Building place concrete slab.
- Concessions Building masonry walls .
- Final grade cuts at sports fields.
- **Baseball/Softball dugout foundations.**
- sidewalk grading weather Dependant.
- complete hard scapes work.
- Continue preparing for Asphalt.

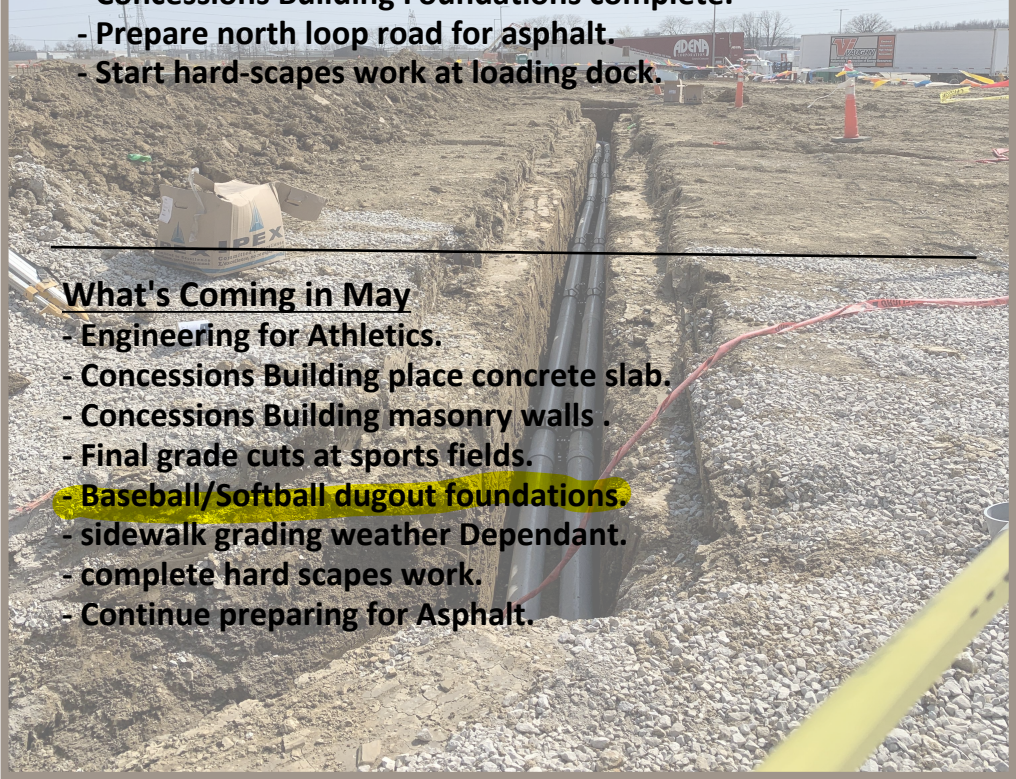


Elementary and Central Energy Plant

What Happened in April

- Commissioning CEP systems.
- place concrete north of CEP.

What's Coming in May

- Central Energy Plant completion.
- **Hydronic piping connections to High school.**





High School

What Happened in April

- All Stairs complete.
- Area 1, 2, 3, 4, 5, 6, 7, 8 flat roofing complete.
- Areas 2 & 7 sloped roof dried in, shingles to follow.
- Area 2 brick veneer underway.
- Courtyard spray foam insulation, brick veneer on going.
- Window frame installation in areas 3, 4, 5 & 6 underway.
- Curtainwall installation starts.
- Area 4, 5 & 6, level 3 wall framing complete.
- Area 4 & 5, levels 1 & 2 Primer & first coat of paint on going.
- Area 4, level 1 & 2 ceiling grid installation on going.
- **Learning stair structural framing started.**

What's Coming in May

- Theater above ceiling systems installation continue.
- continue courtyard finishes.
- Continue Metal Wall Panel installations.
- **continue Mechanical system start up.**
- Roofing finishing.

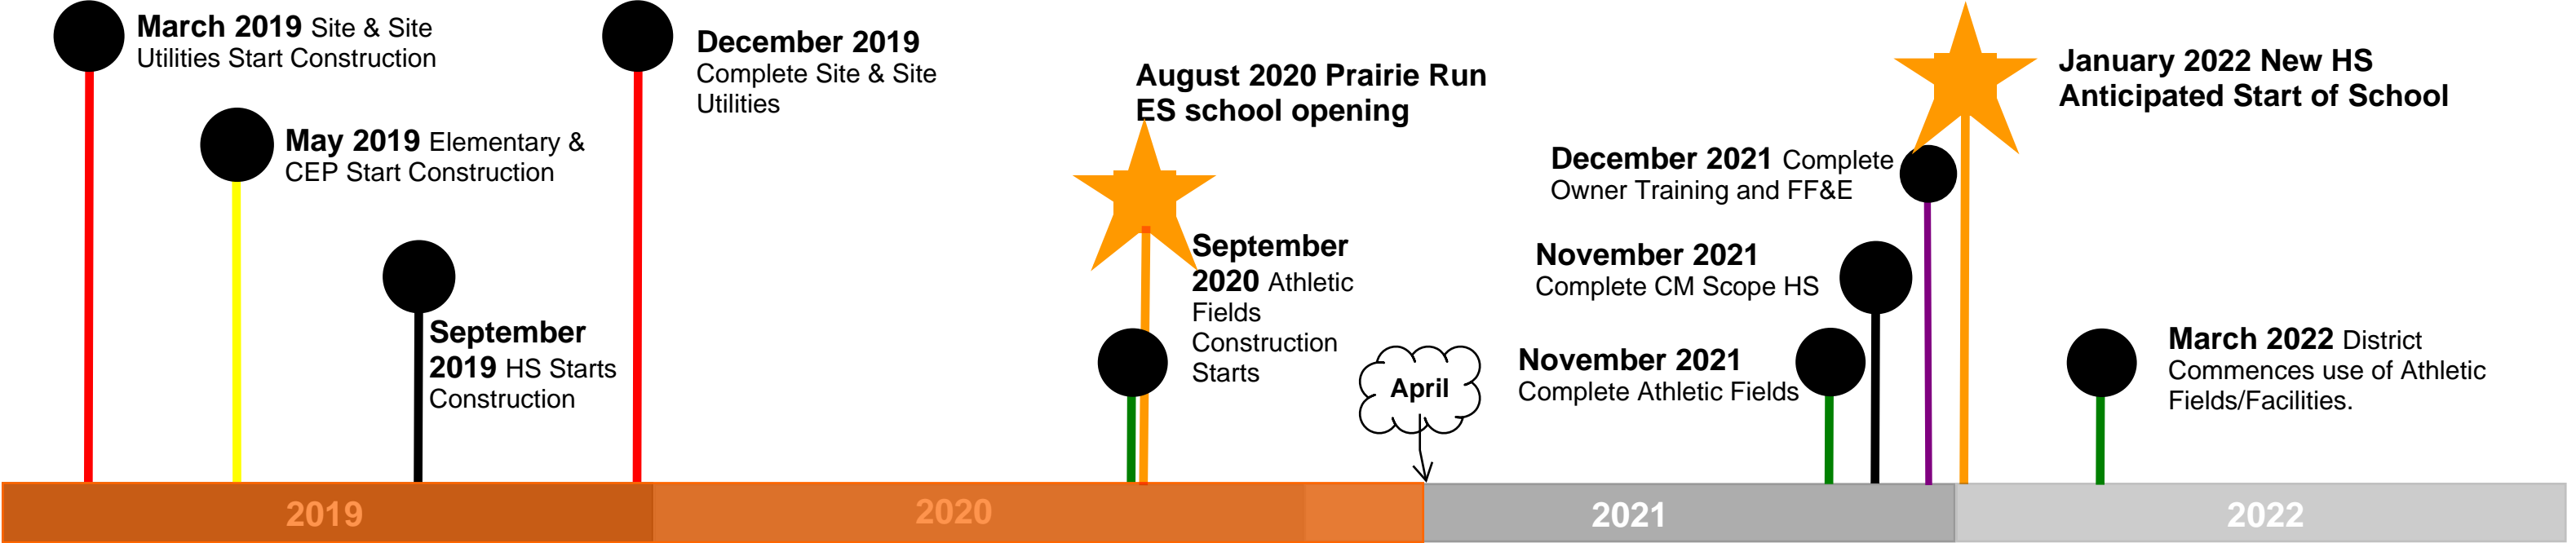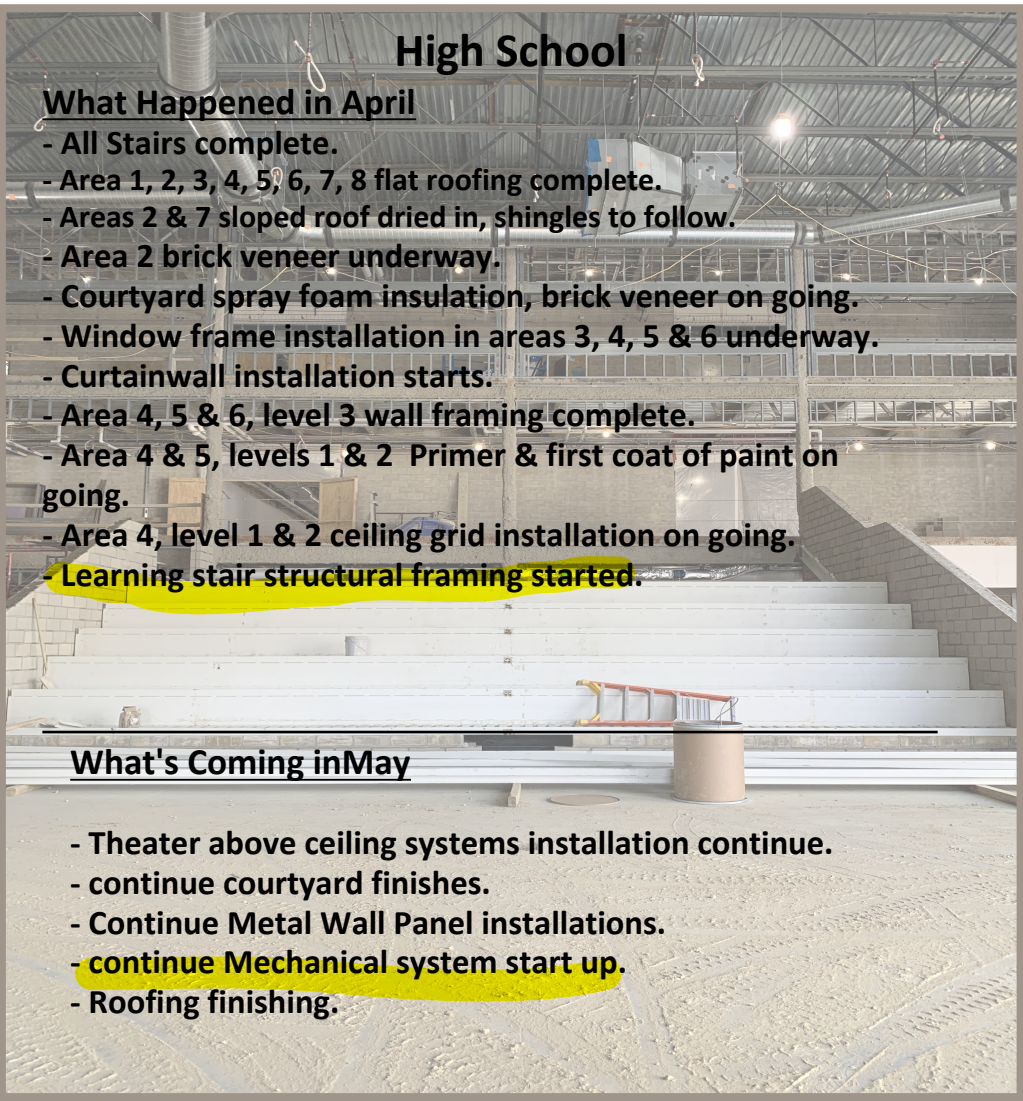

*Note: Final Elementary & HS completion/Move-in dates subject to change pending construction implementation/final inspections
